

Documentation

Anne W. Baker Collection

1973

Mott House: Daily Record

Steve Tyson

Follow this and additional works at: https://docs.rwu.edu/baker_documentation



Part of the [Historic Preservation and Conservation Commons](#)

Recommended Citation

Tyson, Steve, "Mott House: Daily Record" (1973). *Documentation*. 14.
https://docs.rwu.edu/baker_documentation/14

This Documentation is brought to you for free and open access by the Anne W. Baker Collection at DOCS@RWU. It has been accepted for inclusion in Documentation by an authorized administrator of DOCS@RWU. For more information, please contact mwu@rwu.edu.

9/10

STARTED IN 19TH CENTURY ELL. REMOVED JUNK, NUMBERED ALL WOODWORK, STARTED 20TH CENTURY LEANTO (JUST R.F.T.)

9/11 Hand-Dock at Alpine Booth. Put together staining. Recorded woodwork numbering onto prints. Finished 20th cent. leanto, found interesting T&G. 12" boards painted blue (marked LTN 12, 3 etc). Found original 19th cent. dock steps under flooring of leanto.

9/12 Stripped plaster from Kjt rooms, found white washed horizontal planking. Saved nailers from ceiling of ell because of interesting paint, maybe pieced together.

9/13 Stripped shingles from side of ell. Stripped roof of ell. Lifted top flooring, only one small portion seems to be original (right of fireplace). Started removing woodwork from ell. Noted the following: Many pieces of the boarding & flooring seem to come from elsewhere; in J room where original wall should be, is evidenced by 18th cent nails in beam where boarding would have been nailed. Removed sheathing from L room. Found many interesting aspects of framing which will show up in photo's.

9/14 Took bricks out of trailer, finished woodwork in ell. Started chimney. Loaded woodwork marked "X" into trailer.

9/17 Took chim. down to 6 1/2' level, numbered frame, pulled up remaining orig. flooring. Took roofers off, disassembled rafters. Noted window on north wall not original, (frame & sash early). ~~SECRET WINDOW NOT ORIGINAL (FRAME & SASH MISSING)~~. WEST WALL HAS ORIGINAL WINDOWS (DETERMINED BY SASH PLACEMENT)

- 9/18
CONT.
REMOVED HORIZONTAL BOARDING FROM OUTSIDE WALLS, STRIPPED PLASTER FROM 1ST FLOOR N.E. ROOM. REBOARDED BULKHEAD FROM SO. WALL OF ELL - MOSTLY ROTTED, SAWED BOARDS & TOOK MEASUREMENTS OF ROOF ETC. RAINED ALL AFTERNOON (A DAY TO REMEMBER)
- 9/19
STACKED BRICKS FROM OLD CHIMNEY. DISASSEMBLED FRAME, REMOVED NAILS & STACKED TIMBERS, COVRED SAME WITH PLASTIC. REMOVED SUB FLOORING. (ALL IN ELL)
- 9/20
DISASSEMBLED SILL ASSEMBLY, STACKED SAME. SIFTED DIRT FROM CEILING (FOUND COINS, FRAGMENTS OF DILFT, ETC.)
- 9/21
NOTED PEGGED ON VERTICAL PLANKING, IN N.E. Room.
REPAIRED STAIRCHASE, STARTED CHIMNEY, STACKED TIMBERS.
FINISHED SIFTING DIRT IN N.E. Room. SHOVELLED PLASTER FROM N.E. ROOM, THROWN & THREW PUFFARDS (IRON NAILERS IN ROOM THAT WERE ORIGINALLY BUTTERY SHELVES, SAME COLOR GREEN AS IN H ROOM.
- 9/22
NOTED PLASTER BETWEEN VERTICAL BOARDING & PEGGED ON BOARDING ON 18TH CENT., 1ST SECTION. FOUND SHALLOW MOULDED FEATHER BOARD IN "E" SECTION USED AS A NAILER IN 1ST FLOOR CEILING. MARKED WOODWORK IN F, N, C, PR, & ROOMS, RECORDED MARINED WOODWORK IN R, N, O, P, & ROOMS. STRIPPED PLASTER IN E AREA & N.E. LARGER ROOM. REMOVED SOME WOODWORK IN R, F & N AREAS. REMOVED FRONT PORCH.
- 9/23
WORKED ON CHIMNEY, RECORDED NUMBERS IN F Room, NUMBERED & ROOM, REMOVED ATTIC BOARDS (NAILS), SETUP PUMP JACKS. SHOVELLED HALF OF EAST SIDE. FOUND PART OF DOOR FRAME NAILED TO ATTIC WALL (at chimney) WITH REMAINDER OF LEATHER HINGER. NOTICED TIE COLLAR WITH 4-PIG HOLES IN ATTIC, HOLES RESEMBLE PEGGED ON SBATHING HOLES. (111 113)

9/25 BANDED & STORED L ROOM SHEATHING. — ONE BUNDLE. PULLED NAILS
CONT. IN F Room. SHOVELLED PLASTER IN G Room.

9/26 SHOVELLED SHINGLES. STRAPPED PARTITION BOARDS IN ATTIC "P" Room.
STARTED REMOVING FINISH WOODWORK IN F Room, MARKED "M" Room.
LEARNED FORK THAT WAS FOUND IN 1ST FLOOR "E" AREA ~~WAS~~ IS PROBABLY
2ND 1/4 - 18TH C. FOUND INTERESTING BOARD IN F Room WALL, (WEST WALL)
HAVEN'T RESEARCHED IT HS YET. (LOOKS LIKE EMBOSSED BASH PLATE.)


9/27 SHOVELLED SHINGLES, SHOVELLED PLASTER. REMOVED BOARDS IN "M" AREA.
REMOVED WOODWORK IN "F" Room. CLEANED M, F, L & M Rooms.
MANY INTERESTING PATCHES, BOARDS & BOARD LINES WERE SHOVELLED
WITH THE REMOVAL OF SHINGLES, ~~AS~~ AS SHOWN IN PHOTOS.

9/28 REMOVED WOODWORK FROM "F", & IN ROOMS, STACKED & TIED SAME.
STRAIGHTENED OUT TRAILER & STORED WOODWORK FROM "R", "F" & "IN" ROOMS.
SHOVELLED SHINGLES. MORE LINES WERE NOTICED TODAY WHICH INDICATE
17TH C. ROOFLINE WAS IN EXISTANCE WITHOUT CHIM. ON WEST END.
REMOVED LATE LEANTO FROM BEHIND 17TH C. AREA. (WEST END)
SHOVELLED PLASTER OUT OF FOUNDATION HOLE WHERE LEANTO ~~WAS~~ SAT.
NOTICED ^{UNDER} LEANTO ROOF! WHAT WE HAVE THOUGHT WAS WEATHER BOARDS, APPEARS
TO BE JUST HORIZONTAL PLANKING THAT CORRESPOND WITH PLANKING
ON STUDS, AND WERE NOTHING MORE THAN BOARDS THAT RUN PERPENDICULAR
TO VERTICAL BOARDS, & WERE CLAPBOARDED.

10/1 CALLED DEXTER SIEVE. WORKED ON CHIMNEY. SHOVELLED PLASTER FROM HOLE
BEHIND STONE END FOUNDATION. FOUND STONES THAT SEEM TO HAVE BEEN
SOME KIND FOOTING FOR STONE FOUNDATION. THEY ARE FLAT ON GROUND
& RUN UNDER FOUNDATION. REMOVED WOODWORK IN F&IN ROOMS.

10/2 SICK BOTH DAYS, NO CONTACT WITH WORKERS BY PHONE.
10/3 INSTRUCTED THEM TO WORK ON CHIMNEY, WOODWORK & BRICKS.

10/14 CHECKED WORK DONE, EVERYTHING OK, CLEARED ATTIC, 2ND FLOOR.
WORKED BRICKS, REMOVED WOODWORK, DID SOME NUMBERING OF RAFTERS,
MUCH INTERESTING DISCOVERY AS TO WHERE SECOND STORY ROOFLINE
ENDED. FOUND THAT THIS LINE WASN'T PRIMARILY MADE BY
DICK, (NOT SAYING ONE IS WRONG & ONE IS RIGHT) THEREFORE I FEEL
THAT AT THIS POINT IN THE DISASSEMBLY PROCESS, IT IS EXTREMELY
IMPORTANT NOT TO MISS WHAT IT TAKES TO MAKE THIS HOUSE
REASSEMBLED & RESTORED PROPERLY.

10/5 CLEANED & STACKED BRICKS, BANNED STONE. REMOVED WOODWORK & SHEATHING
& STORED IN TRUCK. DREW, NUMBERED & MEASURED DIVIDER BOARDS
AT ATTIC WITH DROPOFF. FOUND POTTERY & LEADED GLASS FRAG-
MENTS. ORIGINAL ATTIC BOARDS ARE BEING REMOVED TO PREVENT
DAMAGED TO THEM, FOUND TWO END BOARDS ON ATTIC THAT
ARE HEAVY AND WALKING SURFACE, ~~THEY ARE~~ REMOVED WOODWORK
IN G ROOM.

10/6 WORKED ON ATTIC FLOORING.

10/9 LOADED ATTIC PLANKING INTO TRUCK. REMOVED WOODWORK IN "G" &
"F" ROOMS. FINISHED SHEETING & SHINGLING GABLE NORTH END.
NUMBERED ALL VERTICAL INTERIOR & END DIVIDER PEGPLATE.

10/10 REMOVED STAIRWAY FROM "P" AREA. REMOVED PLANK WALL FROM "G" ROOM
SIFTED DIRT FROM CHIMNEY HOLES IN 2 ROOMS.

10/11 REMOVED STRINGERS & PLASTER FROM "P" AREA. REMOVED INTERIOR WALLS IN
"G", "P", & "O" AREAS. STABILIZED EXHIBIT BOARDS IN "L" ROOM WITH FINISHING PLYWOOD.
STARTED REMOVING WOODWORK IN "E" AREA. REMOVED BOARD FROM 17TH C. SIDE GIRT.
NOTED THERE WAS NO SIGN OF CLAPBOARDS, NAIL HOLE Holes, VERTICAL PLANKS
OR ANY THING THAT WOULD INDICATE THERE WAS NO STRUCTURE ON
THE REAR OF THE 17TH C. SECTION. FOUND GIANT NAIL CONNECTING
17TH C. & 18TH C. PLATES (@ EAST END AT FRONT DOOR). SPENT

10/11 TAKEN SUPPORTING PLATES & RAFTERS IN ATTIC "T" AREA.

10/12 REMOVED INTERIOR WALLS IN N, J, G, O AREAS. REMOVED FLOORING IN P, Q & C AREAS. REMOVED WOODWORK FROM 1ST FLOOR "E" AREA. FOUND MARK OF 1870C BUTTERFLY HINGE ON TRIM UNDER 1870C TRIM AROUND DOOR IN EARLY 1870C DOORWAY (P.P.P.) ^{DOOR & HINGES} COULD HAVE BEEN FROM LATER 1 STORY E.H. - FINISHED SUPPORTING ATTIC BY RUNNING PURLINS FROM ~~THE~~ CHIMNEY END TO GABLE ENDS. PUT SUPPORTS AT CORNER POSTS WHERE GIRTS & PLATES SIT ON ROTTED POST PENNED, ON SECOND FLOOR.

10/13 STRAPPED & LEADED ALL BOARDS REMOVED ON 10/12. PUT SUPPORTS IN Q ROOM HOLDING RAFTER ONTO PLATE. REMOVED WOODWORK IN SECOND FLOOR "E" AREA. REMOVED STAIRWAY IN "E" AREA (LITTLE STAIRWAY). REMOVED WALLS IN "N" ROOM.

10/15 REMOVED WINDOW FRAMES. FOUND FLINTLOCK HAND GUN UNDER STAIRCASE (FROM "E" INTO "A") REMOVED FLOORING FROM "M" AREA. LEADED WOODWORK & WINDOW FRAMES.

10/16 REMOVED RAFTERS, REMOVED RAFTERS FROM HIGH SECTION OF ROOF. OUTSIDE OF PURLINS, now visible, have strange counter sunk nail holes on INTERNAITON & RAFTERS. THEY APPEAR TO HAVE BEEN DONE WITH HALF-Round NAILS. 

10/17 REMOVED SHEATHING FROM "H" ROOM, FOUND THREE PIECES OF EASEMENT FRAMES ^{4"} FOR SASH. REMOVED HALF OF 1870C RAFTER TRUSSES.

10/18 REMOVED REMAINDER OF ROOF. ON 1870C ROOF. DENAILED RAFTERS

10/19 CLEANED ROOFERS FROM REAR HOUSE. SAVED GOOD ONES (ABOUT 30%) DENAILED "H" ROOM SHEATHING, STACKED, STRUNG, & STORED SAME.

10/23 SIFTED DIRT FROM AROUND CHIMNEY AREA (FOUND MANY INTERESTING PIECES OF GLASS, LEATHER, WOOD & REDIVAR). BANDED PLANKS FROM ATTIC OF EAST VERTICAL WALL. REMOVED MOST OF FLOORING FROM ATTIC ON 18THC SIDE, & DENAILED SAME.


10/24 FINISHED REMOVING ATTIC FLOORING. NUMBERED FLOOR TOISTS IN N, O, P & Q CEILING AREAS. CLEANED "A" ROOM & PLACED ARROWS FOR JAN'S PICTURES. REMOVED SHEATHING FROM "B" AREA. DISCOVERED STRANGE MARKS ON OUTSIDE & IN "A" DOORWAY AREA (EXT. CHAM. ON POST ETC.) BANDED & STORED ALL ATTIC FLOORING. DENAILED ROOFERS.

10/25 REMOVED ALL REMAINING INTERIOR WOODWORK & WALLS, BANDED & STORED SAME. REMOVED FLOOR TOISTS IN N, O, P & Q AREAS, REMOVED ALL EXTERIOR PLANKING FROM 2ND & 18THC SECTION. REMOVED LEANTO FROM BACK OF 18THC SECTION. DENAILED & BANDED ALL FLOOR TOISTS. FOUND EVIDENCE THAT LEANTO WAS ORIGINAL TO 18THC ADDITION. FOUND POCKET IN "H" ROOM S-W. POST THAT PROTRUDES SOMETHING EXTENDED SOUTH ORIGINALLY. THE GLESS AT THIS POINT IS SOME KIND OF DOORWAY OR ENTRANCE.


10/26 SURVIVED & BANDED REAR PLATE OF 18THC SECTION. REAR PLATES & GIRTS TO BE INVOLVED IN DISASSEMBLY. SECURED ALL POSTS & PLATES OF 18THC ADDITIONALLY. STARTED DISASSEMBLY IN THE FOLLOWING MANNER: REMOVED ROOFERS FROM LEANTO; REMOVED RAFTERS; REMOVED FLOOR TOISTS; OUTSIDE PLATE; POSTS; AT THIS POINT WE WENT UPSTAIRS & REMOVED OUTSIDE REAR PLATE, SECURED REAR GIRT. REMOVED SUB FLARING IN O, P, Q AREAS, REMOVED TOISTS IN SAME AREAS. TIRED S.W. POST IN SOUTHERLY DIRECTION & REMOVED SOUTH-WEST SIDE GIRT; REMOVED S. END GIRT & S.W. POST. MOVED WEST POST IN WESTERLY DIRECTION & LOWERED CENTER GIRT. REMOVED NW. SIDE GIRT; A POST & N. SIDE GIRT CAME NEXT. FINALLY CAME THE ENTIRE EAST SECTION (ONE STORY) DROPPED IN ONE PIECE. (SEE NEXT PAGE FOR DESCRIPTION.)

10' x 26' OBSERVATION AT 18.75' C 2 STORY HOTEL ADDITION.

→ WEST

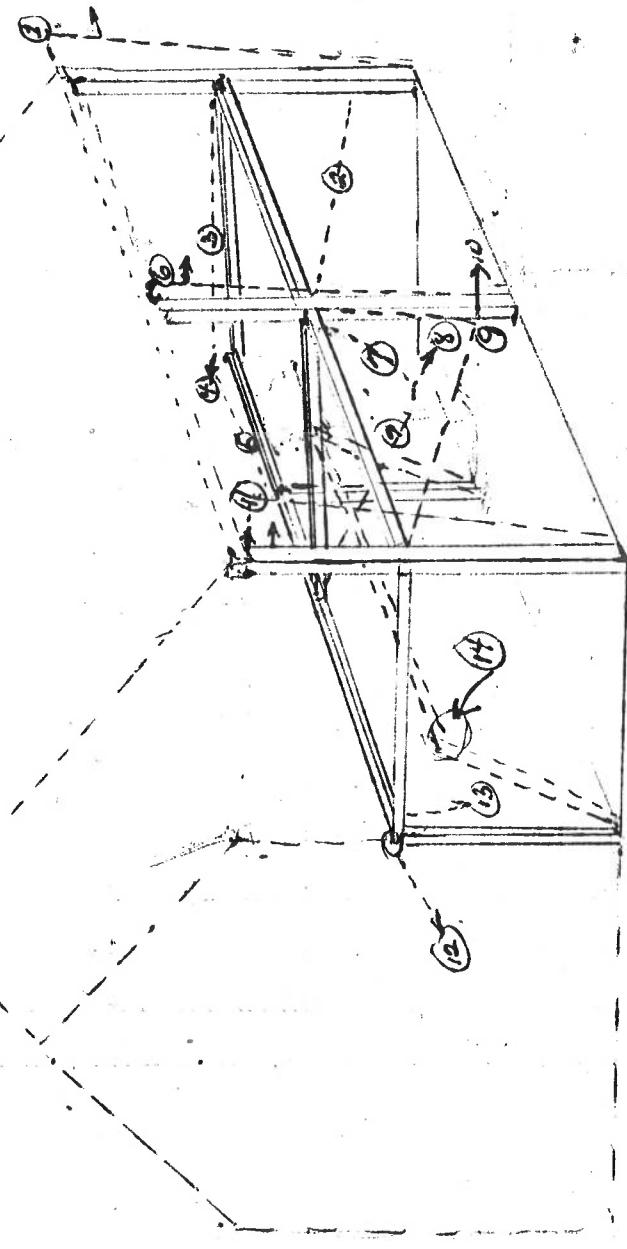

- 10/27 LIFTED FLOORING IN "E" AREA TO FIND SILLS. FOUND THAT SILLS
CONTINUE FROM REAR OF EARLY 18TH C. SECTION TO SIDE OF LEANTER.
FOUND POCKET IN POST (N.W. EARLY SECTION) THAT INDICATES
SOMETHING PRECEDED 2 STORY ADDITION.
- 10/28 SHIELDED FIREPLACE IN "F" ROOM, DENAILED SIDING & TIMBERS - RAINED
OUT AT NOON.
- 10/30 RAINED OUT TIL NOON (2 MEN WORKED 11:30 AM) DRAW SUPPORTS
ON INSIDE & OUTSIDE CLAPBOARDED ^{WEST} WALL OF 18TH C. SECTION,
PROTECTED CLAPBOARDS WITH PLYNED. SAWED PLANKS IN HALF AT
GIRLS & REMOVED. REMOVED MOST OF PLANKING IN 18TH C.
SECTION.
- 10/31 REMOVED STAIRWAY, FOUND DOUBLE TRENDE ON EVERY STEP. FINISHED
REMOVING VERTICAL PLANKING IN 18TH C. SECTION. STARTED
REMOVING FLOORING IN EHT. REMOVED FLOOR JOISTS IN EHT. IN 18TH C. SECTION
STARTED REMOVING SECOND STORY PLATES & GIRLS IN 18TH C. SECTION.
- 11/1 BRACED & SUPPORTED TIMBERS IN 18TH C. SECTION. RAIN & WIND
NOT CAN ON MOST OF DAY.
- 11/2 ROLLED UP FLOORING IN EHT, 2ND FLOOR. DENAILED & BOARDED
PLANKING, FLOORING, JOISTS. BRACED 1ST FLOOR ^{1ST} TIMBERS. REMOVED
EAST & WEST 18TH C. PLATES. REMOVED FLOORING IN "H" AREA.
REMOVED FLOOR JOISTS IN SAME AREA. DISASSEMBLED 18TH C. FRAMES
AS SHOWN ON FOLLOWING PAGE.

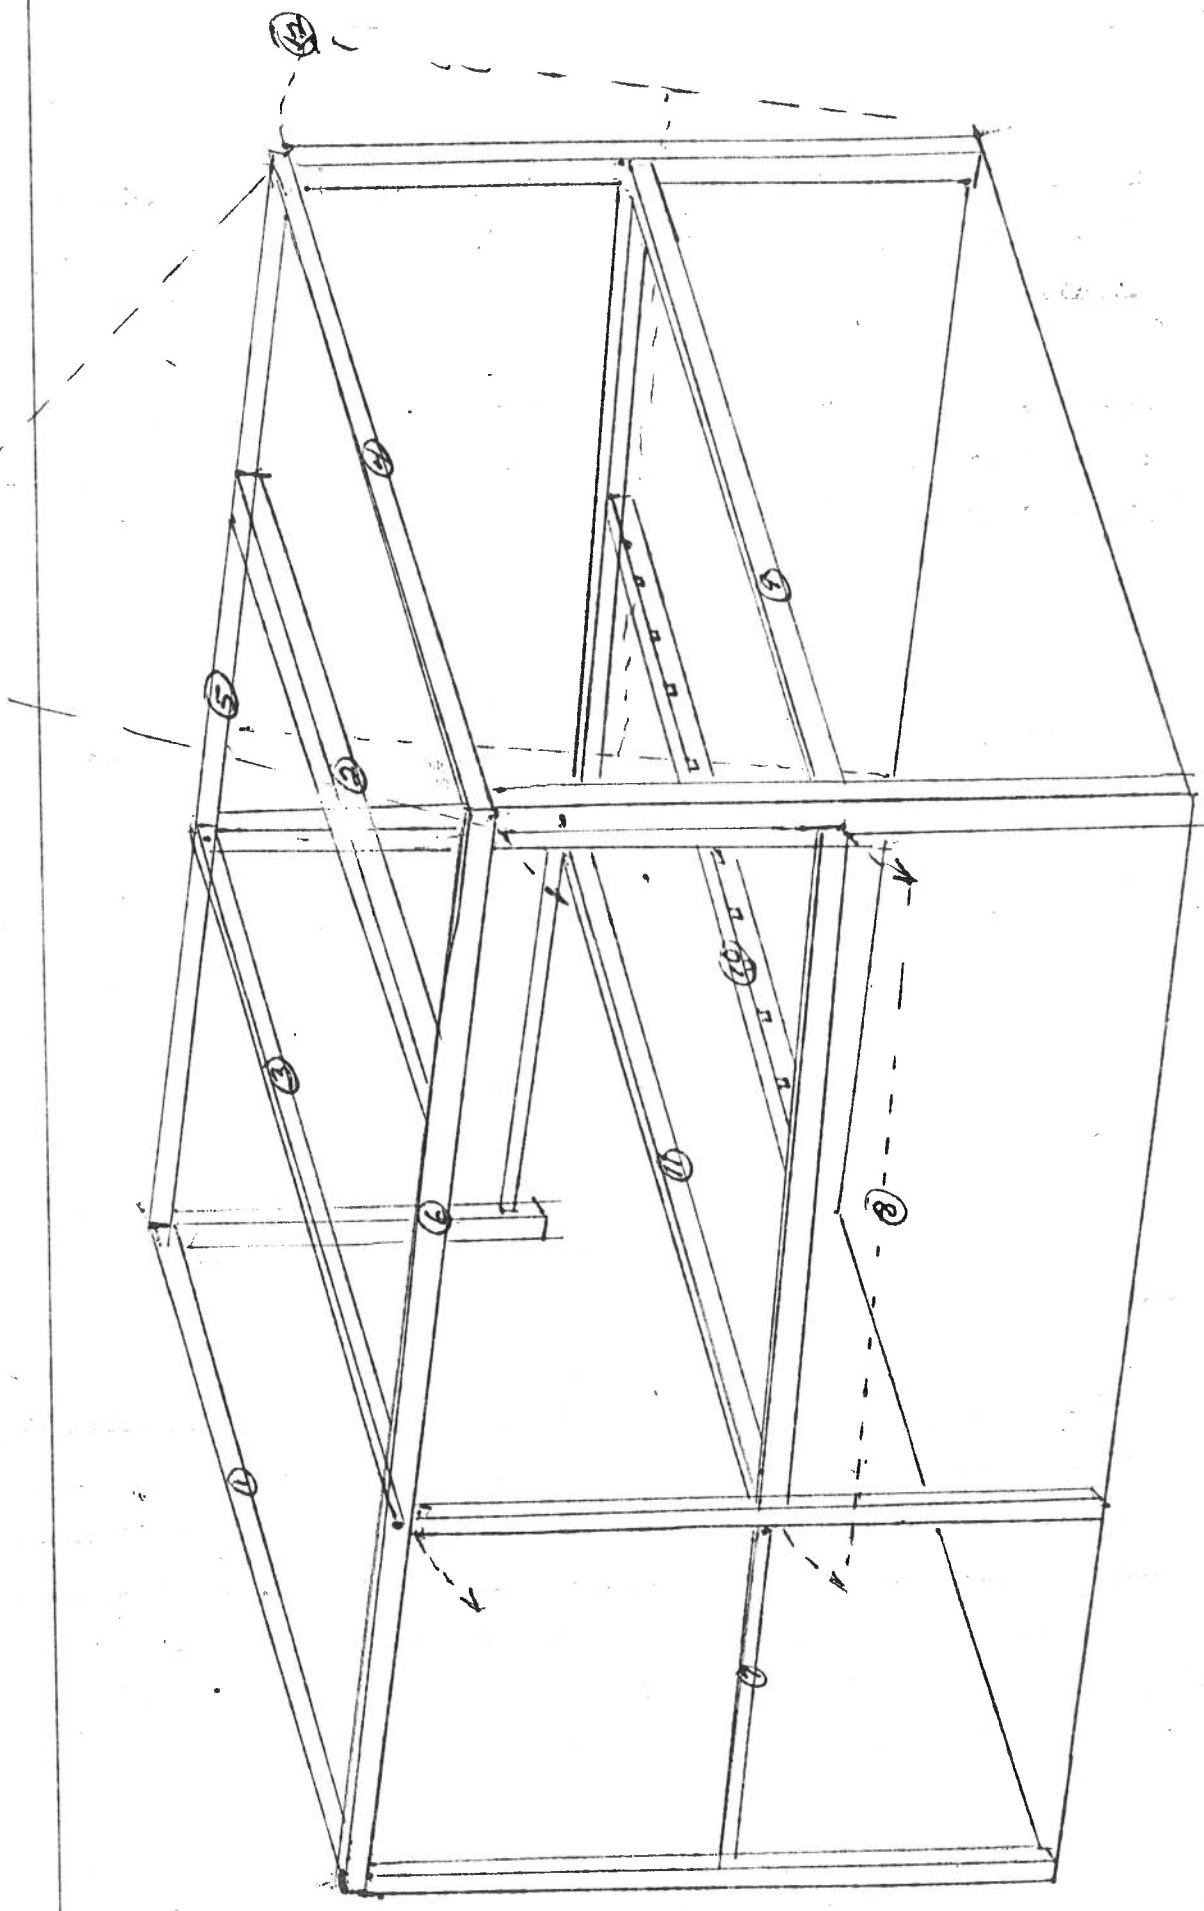

11/3 REMOVED PERLINS, RAFTERS FROM "EHT". REMOVED FLOOR BOARDS
IN EHT ON "L" AREA. REMOVED TOP, E' SUB FLOORING IN A, J, E' &
A BEAMS.

11/5 BANDED, DENAIRED & LOADED ALL FLOORING, SHEATHING, MOULDING, ETC.
REMOVED HORIZONTAL PLANKING ON SOUTH-WALL. REMOVED
FLOORING IN EHT. LOADED Box - DON DELIVERED FLATBED & Tool Box.

11/6 REMOVED REMAINING PLANKING & WEATHER BOARDING IN EHT. PROTECTED
BANDED TIMBERS WITH FIRING BANDS. NUMBERED STUDS ETC. IN
EHT. REMOVED FLOOR JOISTS, IN EHT, & 18.40 AREA. DROVE PINS
TO PREPARE FRAME FOR CRANE.

11/7 IT'S DOWN!!! CRANE ARRIVED AT 8:30. AT 3:30 P.M.,
THE EHT WAS IN THE FLATBED. EVERYTHING CAME APART
SMOOTHLY. NO BREAKAGE! THE EAT WAS DISASSEMBLED IN
THE FOLLOWING WAY: REMAINING RAFTERS WERE
DISASSEMBLED EXCEPT FOR LARGEST SET. (LOWED FIRST)
REMOVED BOARDING, FLOORING, FLOOR JOISTS. THE FRAME
WAS REMOVED ~~IN~~ THIS MANNER: TIE BEAMS FIRST,
WEST SUMMER. ① STONE END GIRT ② CHIM. GIRT. ③ WEST
SUMMER ④ END GIRT. ⑤ NORTH PLATE ⑥ SOUTH PLATE ⑦ ALL
STUDS, NAILERS & 1 STORY POSTS ON SECOND FLOOR. BACK SECTION (WES
THAT HEAD IN CHIMNEY WAS TAKEN NEXT: S.W. POST, WEST GIRT,
N.W. POST. THEN CAME THE REMAINDER AS FOLLOWS: CRANE
HOLD UP EAST END GIRT, ① BOTH 1-STORY POSTS WERE REMOVED,
② END GIRT WAS NEXT, THEN ③ SUMMER ④ NORTH SIDE
GIRT ⑤ SOUTH SIDE GIRT ⑥ SOUTHWEST 2-STORY POST,
⑦ CHIM GIRT ⑧ N.W. 2-STORY POST.

11/8 LOADED FLATBED USING CRANE TO REMOVE SILLS &
FLOOR JOISTS. (House complete at this point) THEN
LOAD BOARD

(C)

4/9 SUPPORTED FIRE PLACE. LOADED PLANKS & DELIVERED TO EAST GREENWICH.

4/10 TRANSFERRED RAISED PANELING FROM 1 GARAGE TO ANOTHER.
BROUGHT ODDS & ENDS TO EAST GREENWICH.

(D)

TRUCK
UNLOADING

3.50
x 8
\$28.00

Amount for $\frac{1}{2}$ previous

CHEM LISANKO
128 DOYLE AVE.
PROVIDENCE, R.I.

\$28.00 ✓ -

DEL UPTON
166 BURGESS AVE
EAST PROVIDENCE

\$28.00 ~~\$~~ \$20?

EDWARD Mc GUIRE
292 AQUEDUCT RD.
CRANSTON, R.I. 02910

\$28.00 ✓ -

ROBERT BARKER
40 FLORENCE ST.
PAWTUCKET R.I.

\$28.00 ✓ -

RAYMOND SANGIOVANNI
55 GREEN RIVER AVE.
WARWICK, R.I. 02889

\$28.00 V
\$140.00

SUBTOTAL

STEVE TYSON
46 GREEN RIVER AVE
WARWICK, R.I. 02889

3.50
3.50

68.00 ~~n~~

1120
28

ELEANOR CARRIERE
19 VALE ST.
PROVIDENCE

3.50

208.00 ~~for 22~~
195.00 ~~for 22~~

\$403.00

155

TOTAL RECK \$195

WEEK ENDING 9/15 - 765

NAME	PER HR.	MON.	TUES.	WED.	THURS.	FRI	TOTAL
ERNIE BELLAIRE		8	8	8	8	8	40
DICK CARRIERE		1	5	1	1	1	11
CHEM LISANKE*		1	1	1	1	1	5
ED MC GURL		1	1	1	1	1	6
PETE BAKER		1	1	1	1	1	6
STEVE TYSON		8	8	8	8	8	40

*CARE TAKER

NAME	PER HR.	MON.	TUES.	WED.	THURS.	FRI	TOTAL
ERNIE BELLAIRE		8	8	8	8	8	40
DICK CARRIERE		1	1	1	1	1	4
CHEM LISANKE*		1	1	1	1	1	5
ED MC GURL		1	8	1	1	1	4
PETE BAKER		1	1	1	1	1	4
DEL UPTON		1	1	1	1	1	4
JIM PARLIN		1	1	1	1	1	4
STEVE TYSON		8	8	8	8	8	40
NAME	PER HR.	MON.	TUES.	WED.	THURS.	FRI	TOTAL
ERNIE BELLAIRE		8	8	8	8	8	40
ED MC GURL		8	8	8	8	8	40
PETE BAKER		8	8	8	8	8	40
JIM PARLIN		1	1	1	1	1	4
DEL UPTON		1	1	1	1	1	4
CHEM LISANKE*		1	1	1	1	1	5
GERALD PAYETTE		8	8	8	8	8	40
STEVE TYSON		8	8	8	8	8	40

* CARE TAKER

NAME	MON.	TUES.	WED.	THURS.	FRI	TOTAL
WEEK ENDING 10/6						
ERINIE BELLAIRE	8	E	E	E	8	40
ED MCGIRL	8	E	E	4	40	
PETE BAKER	-	-	-	-	7	
JIM PARKIN	-	-	-	8	8	
DEL UPTON	8	8	8	8	8	30
CLEM LISSANKE*	8	8	8	8	8	40
STEVE TYSON	8	8	8	8	8	35
10/13						
ERINIE BELLAIRE	X	8	8	8	8	40
ED MCGIRL	X	8	8	8	8	32
PETE BAKER	-	-	-	-	6	
JIM PARKIN	-	-	-	-	-	14 1/4
DEL UPTON	X	8	8	8	8	40
CLEM LISSANKE*	#	#	8	10	10	40
STEVE TYSON	#	8	8	8	8	40
10/20						
ERINIE BELLAIRE	8	8	8	8	8	40
ED MCGIRL	8	8	8	8	8	40
PETE BAKER	-	-	-	-	6	
JIM PARKIN	-	-	-	8	8	
DEL UPTON	8	8	8	8	8	40
CLEM LISSANKE*	8	8	8	8	8	40
STEVE TYSON	8	8	8	8	8	40

NANIE

FRANCIS BERNARD

For McGehee

Pete BAKER

Tim Berlin

Rev. 1/27/01

CLEM LANGEKIE

THE SUN

ALL DAY

卷之三

ERNE BELLAIKE

Ed McGuirk

PETE PARKER

Tim Perrin

Rev. 1970

CLEM KISANGET

www.TutorVista.com

—ANDREW REEDLEY

—
—

—
—

ERNE BELHAIRE

ED McGURK

Pete BAKER

The Poetry

DEL VPOAN

DEM LISA NKE*

SPRING TUBSON

GRADING BUCKEY

	SUN.	TUES.	WED.	THURS.	FRI.	SAT.	TOTAL
16	8	8	8	8	8	-	32
17	8	-	8	8	-	-	24
Holiday	-	-	-	-	-	-	-
Holiday	8	8	8	8	8	-	32
Holiday	8	8	8	8	8	-	32
Y	8	8	8	8	8	8	48
4 1/2	3 1/2	-	-	5	-	-	20 1/2

ERNE BELLARE
ED MCGUIRE
PETE PARKER
JIM PARKIN
DEA UPTON
CLEM LISANKET
STEVE TYSON
GERALDINE BECKER

WEEK	END NO.	11/3	30
6	8	8	30
6	8	8	30
6	6	8	14
6	-	-	-
6	-	-	-
6	-	-	40
6	8	8	8
6	8	8	8
6	+	8	30
6	8	8	14
6	6	8	48
6	8	8	11
6	-	-	144

ERNIE BELNAIRE
ED MCGUIRE
PETE BAKER
TOM PARKIN
DEB UPTON
CATHY LISANKIE*
STEVE TYSON
GERALDINE BUCKLEY
